

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Notes	Resource Names	Half 2, 2017							Half 1, 2018								
									M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
1		NODOS/Sites Reservoir Project Schedule - Preliminary Draft Subject to Change	1341 days	Fri 1/18/19	Fri 3/8/24																			
2		CEQA/NEPA Process	1341 days	Fri 1/18/19	Fri 3/8/24																			
3		Reclamation - Waivers	1341 days	Fri 1/18/19	Fri 3/8/24			Reclamation																
11		Authority - Draft Project Description and Annotated Outline	218 days	Wed 4/1/20	Fri 1/29/21																			
12		Authority prepare Preliminary Draft Project Description	109 days	Wed 4/1/20	Mon 8/31/20		P6 EIR - 010	Consultants																
13		Authority prepare Annotated Outline and Introduction Chapter	109 days	Wed 4/1/20	Mon 8/31/20		P6 EIR - 015	Consultants																
14		Authority/Reclamation review of the Prelim. Draft Project Description and Annotated Outline	16 days	Tue 9/1/20	Tue 9/22/20	12,13		Authority,Integration,Rec																
15		Authority prepare Revised Draft EIR/SDEIS Project Description Chapter	69 days	Wed 9/23/20	Mon 12/28/20	14	P6 ID EIR - 021	Consultants																
16		Authority Ad Hoc Environmental Planning and Work Group Permitting Briefing Revised Draft EIR/SDEIS Project Description	0 days	Thu 12/17/20	Thu 12/17/20	15FS-10 days		Authority,Integration,Cor																
17		Final Revised Draft EIR/SDEIS Project Description to Authority Ad Hoc EPP Work Group, Reservoir Comm., and Board for Review and Approval to Post	15 days	Mon 1/11/21	Fri 1/29/21	15FS+9 days		Authority,Integration,Cor																
18		Complete Revised Draft EIR/SDEIS Project Description Chapter	0 days	Fri 1/29/21	Fri 1/29/21	17																		
19		Reclamation SDEIS Development Clearance	25 days	Wed 11/4/20	Tue 12/8/20			Reclamation																
27		Authority/Reclamation Revised Draft EIR/SDEIS Development	223 days	Mon 9/14/20	Wed 7/21/21																			
28		Reclamation - Refine Plan for SDEIS	60 days	Wed 9/16/20	Tue 12/8/20			Reclamation																
33		Reclamation - NEPA Cooperating Agency Coordination	58 days	Mon 9/14/20	Wed 12/2/20			Reclamation																
40		Authority/Reclamation Team Admin. Revised Draft EIR/SDEIS Development	223 days	Mon 9/14/20	Wed 7/21/21																			
41		Reclamation Compile List of Reviewers by subject matter	30 days	Mon 9/14/20	Fri 10/23/20			Reclamation																
42		Authority Water Modeling	37 days	Mon 11/23/20	Tue 1/12/21			Reclamation																
43		USRDOM	31 days	Mon 11/23/20	Mon 1/4/21																			
44		HEC-5Q & RecTemp	31 days	Mon 11/23/20	Mon 1/4/21																			
45		Fish Mortality (Anderson & Martin)	31 days	Mon 11/23/20	Mon 1/4/21																			
46		SALMOD, SalMort, & RecMort	31 days	Mon 11/23/20	Mon 1/4/21																			
47		DSM2 (Hydro & Qual)	31 days	Mon 11/23/20	Mon 1/4/21																			
48		IOS & DPM (Cramer)	31 days	Mon 11/23/20	Mon 1/4/21																			
49		OBAN (QEDA)	31 days	Mon 11/23/20	Mon 1/4/21																			
50		Mercury (RBI)	37 days	Mon 11/23/20	Tue 1/12/21																			
51		Reservoir Water Quality	37 days	Mon 11/23/20	Tue 1/12/21																			
52		Power (LTGen, SWP Power, & Sites Power)	37 days	Mon 11/23/20	Tue 1/12/21																			
53		Water Supply Economic (SWAP & CWEST) (as needed)	37 days	Mon 11/23/20	Tue 1/12/21																			
54		Water Quality Economics (BAWQM & LCRBWQM) as needed)	37 days	Mon 11/23/20	Tue 1/12/21																			
55		Operations Analysis for Admin. Revised EIR/SDEIS	0 days	Mon 1/4/21	Mon 1/4/21	46,43,44,45,		Consultants																
56		Full Operations Analysis Complete	0 days	Tue 1/12/21	Tue 1/12/21	54																		
57		Authority Prepare Admin. Revised Draft EIR/SDEIS Analysis (Batch 1 Construction)	57 days	Wed 9/23/20	Thu 12/10/20	14	P6 ID EIR - 019	Consultants																
58		Authority/Reclamation review of the Admin. Revised Draft EIR/SDEIS Analysis (Batch 1 Construction)	15 days	Fri 12/11/20	Thu 12/31/20	57		Authority,Integration,Rec																
59		Authority Prepare Admin. Revised Draft EIR and Supp. EIS Analysis (Batch 2 Operations)	63 days	Mon 1/4/21	Wed 3/31/21	57,55FS-1 day	P6 ID EIR - 020	Consultants																
60		Authority Prepare Cumulative and Climate Change Section	79 days	Fri 12/11/20	Wed 3/31/21	57		Consultants																
61		Authority/Reclamation Compile/Prepare Admin Revised Draft EIR/SDEIS	135 days	Thu 9/24/20	Wed 3/31/21	14	P6 ID EIR - 030. This section needs to be expanded to include	Authority,Integration,Rec																
62		Complete Admin. Revised Draft EIR/SDEIS	0 days	Wed 3/31/21	Wed 3/31/21	61																		
63		Authority Ad Hoc EPP Work Group, Reservoir Comm., and Board Status Update on the Admin. Revised Draft EIR/SDEIS	11 days	Thu 4/15/21	Thu 4/29/21	61FS+10 days	P6 ID EIR - 023	Authority,Consultants,Int																
64		Authority review of Admin Revised Draft EIR/SDEIS	22 days	Thu 4/1/21	Fri 4/30/21	61	P6 ID EIR - 035	Authority,Integration																
65		Reclamation SME review of Admin. Revised Draft EIR/SDEIS (and cooperating agencies as applicable)	30 days	Thu 4/1/21	Wed 5/12/21	61	Where does FWCA and PAM fit in?	Reclamation																


Project: DRAFT_Sites_Constrain
Date: Tue 10/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Notes	Resource Names	Half 2, 2017							Half 1, 2018								
									M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
66		Authority incorporate comments/edits and prepare Revised Draft EIR/SDEIS	22 days	Mon 5/3/21	Tue 6/1/21	64	P6 ID EIR - 040	Consultants																
67		Authority/Reclamation Live Edit Revised Draft EIR/SDEIS meeting (SMEs and cooperating agencies)	1 day	Wed 6/2/21	Wed 6/2/21	66	P6 ID EIR - 045	Authority,Integration,Rec																
68		Authority Legal review of Revised Draft EIR/SDEIS	15 days	Thu 6/3/21	Wed 6/23/21	67	P6 ID EIR - 050	Authority																
69		Authority Ad Hoc EPP Work Group, Reservoir Comm., and Board Briefing on the Public Revised Draft EIR/SDEIS	12 days	Tue 6/15/21	Wed 6/30/21	68FS-7 days		Authority,Consultants,Int																
70		Authority resolve Legal Comments on Revised Draft EIR/SDEIS	10 days	Thu 6/24/21	Wed 7/7/21	68	P6 ID EIR - 060	Authority																
71		Authority/Reclamation Live Edit Revised Draft EIR/SDEIS meeting after legal comments	0 days	Wed 7/7/21	Wed 7/7/21	70	P6 ID EIR - 065	Authority,Integration,Rec																
72		Authority Final Editing, Formatting, and Document Production	10 days	Thu 7/8/21	Wed 7/21/21	70	P6 ID EIR - 067	Authority,Consultants																
73		Authority Ad Hoc Environmental Planning and Permitting Work Group Final Briefing of Public Draft Revised EIR/SDEIS	1 day	Thu 7/15/21	Thu 7/15/21	72FS-5 days		Authority																
74		Authority Reservoir Committee Final Briefing of Public Draft Revised EIR/SDEIS and provide recommendation to Authority Board for the release of the Public Draft Revised EIR	1 day	Fri 7/16/21	Fri 7/16/21	73	3rd Friday of the month; could have a special Res. Comm. Mtg	Authority																
75		Special Authority Board Meeting for approval to release the Draft Revised EIR for Public Review	1 day	Mon 7/19/21	Mon 7/19/21	74	P6 ID EIR - 070; 4th Wed. of the month; could have special Board	Authority																
76		Complete Public Revised Draft EIR/SDEIS	0 days	Wed 7/21/21	Wed 7/21/21	72																		
77		Reclamation - Revised Draft EIR/SDEIS Clearance for Public Release	24 days	Thu 7/22/21	Tue 8/24/21																			
86		Authority/Reclamation - Revised Draft EIR/SDEIS Public Release	68 days	Thu 7/22/21	Mon 10/25/21																			
87		Publish Revised Draft EIR/SDEIS	28 days	Thu 7/22/21	Mon 8/30/21																			
88		Prepare SDEIS letter (optional), press release, and Public Notice (for Reclamation website and newspapers)	20 days	Thu 7/22/21	Wed 8/18/21	76	Need to run press release through DC so plan adequate time. Make	Reclamation																
89		File SDEIS with EPA	0 days	Tue 8/24/21	Tue 8/24/21	85	EPA publishes NOAs ONLY on F	Reclamation																
90		SDEIS NOA Published in Federal Register	4 days	Wed 8/25/21	Mon 8/30/21	89		Reclamation																
91		Publish SDEIS, SDEIS letter (optional), public notice on Reclamation Website; issue press release	0 days	Tue 8/24/21	Tue 8/24/21	85		Reclamation																
92		Update OEPC Database	0 days	Tue 8/24/21	Tue 8/24/21	85		Reclamation																
93		Public Review	68 days	Thu 7/22/21	Mon 10/25/21																			
94		Public Review of Revised Draft EIR/SDEIS	44 days	Wed 8/25/21	Mon 10/25/21	85	60 calendar days; Recommend beg																	
95		Prepare materials for Revised Draft EIR/SDEIS public meeting or hearing	38 days	Thu 7/22/21	Mon 9/13/21	76		Authority,Integration,Rec																
96		Hold public meeting #1	12 days	Tue 9/21/21	Wed 10/6/21	94FS-25 day		Authority,Consultants,Int																
97		Hold public meeting #2	13 days	Tue 9/28/21	Thu 10/14/21	94FS-20 day		Authority,Consultants,Int																
98		Prepare Final EIS and Draft ROD	115 days	Wed 8/25/21	Tue 2/1/22																			
112		FEIS Clearance for Public Release	20 days	Tue 2/1/22	Mon 2/28/22																			
121		Public Release of Final EIS	46 days	Wed 2/2/22	Wed 4/6/22																			
130		Prepare Final ROD	45 days	Tue 3/1/22	Mon 5/2/22																			
134		ROD Clearance (Depends on construction appropriation)	246 days	Fri 7/1/22	Mon 6/12/23																			
147		Public Release of ROD	25 days	Tue 5/9/23	Mon 6/12/23																			
153		National Historic Preservation Act Consultation	703 days	Thu 10/1/20	Mon 6/12/23																			
156		Endangered Species Act Consultation	706 days	Mon 8/17/20	Mon 5/1/23																			
178		Geotechnical Investigations	732 days	Mon 7/27/20	Tue 5/16/23																			
221		Definite Plan Report	445 days	Mon 4/5/21	Fri 12/16/22																			

Project: DRAFT_Sites_Constrain
Date: Tue 10/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

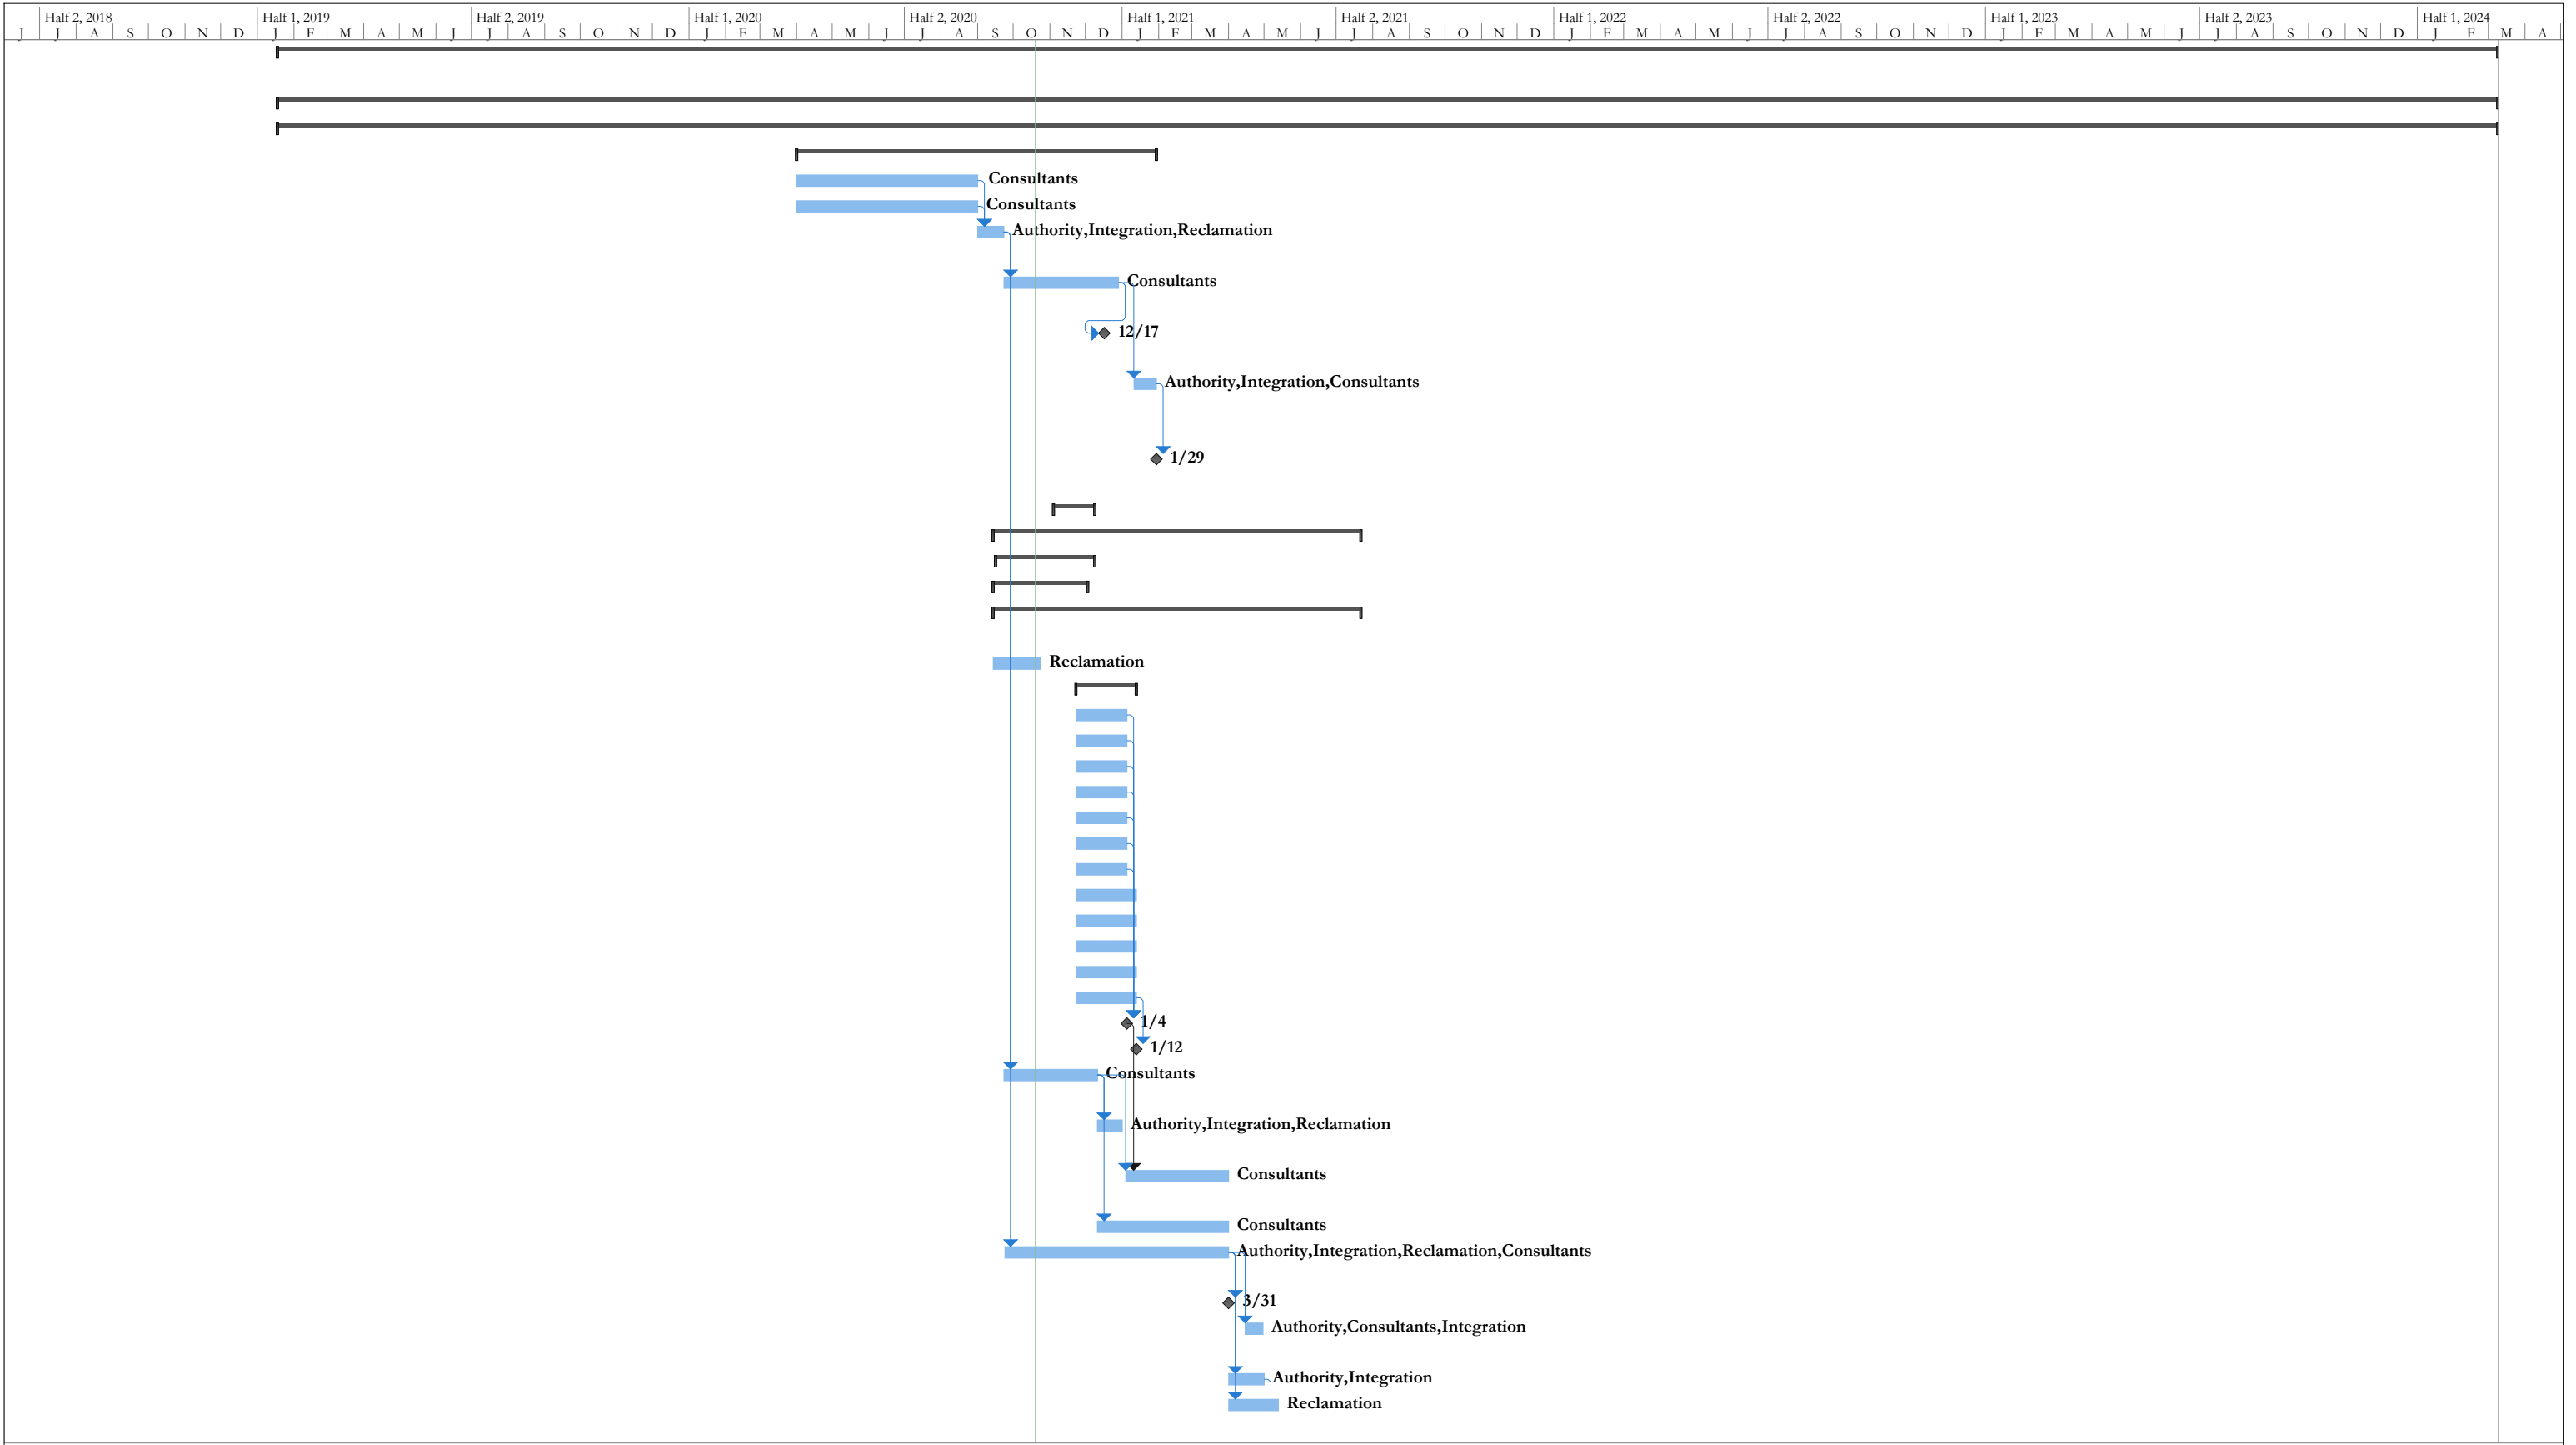

Project: DRAFT_Sites_Constrain Date: Tue 10/20/20	Task	Summary	Inactive Milestone	Milestone	Duration-only	Start-only	External Milestone	Manual Progress
	Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress	
	Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks			

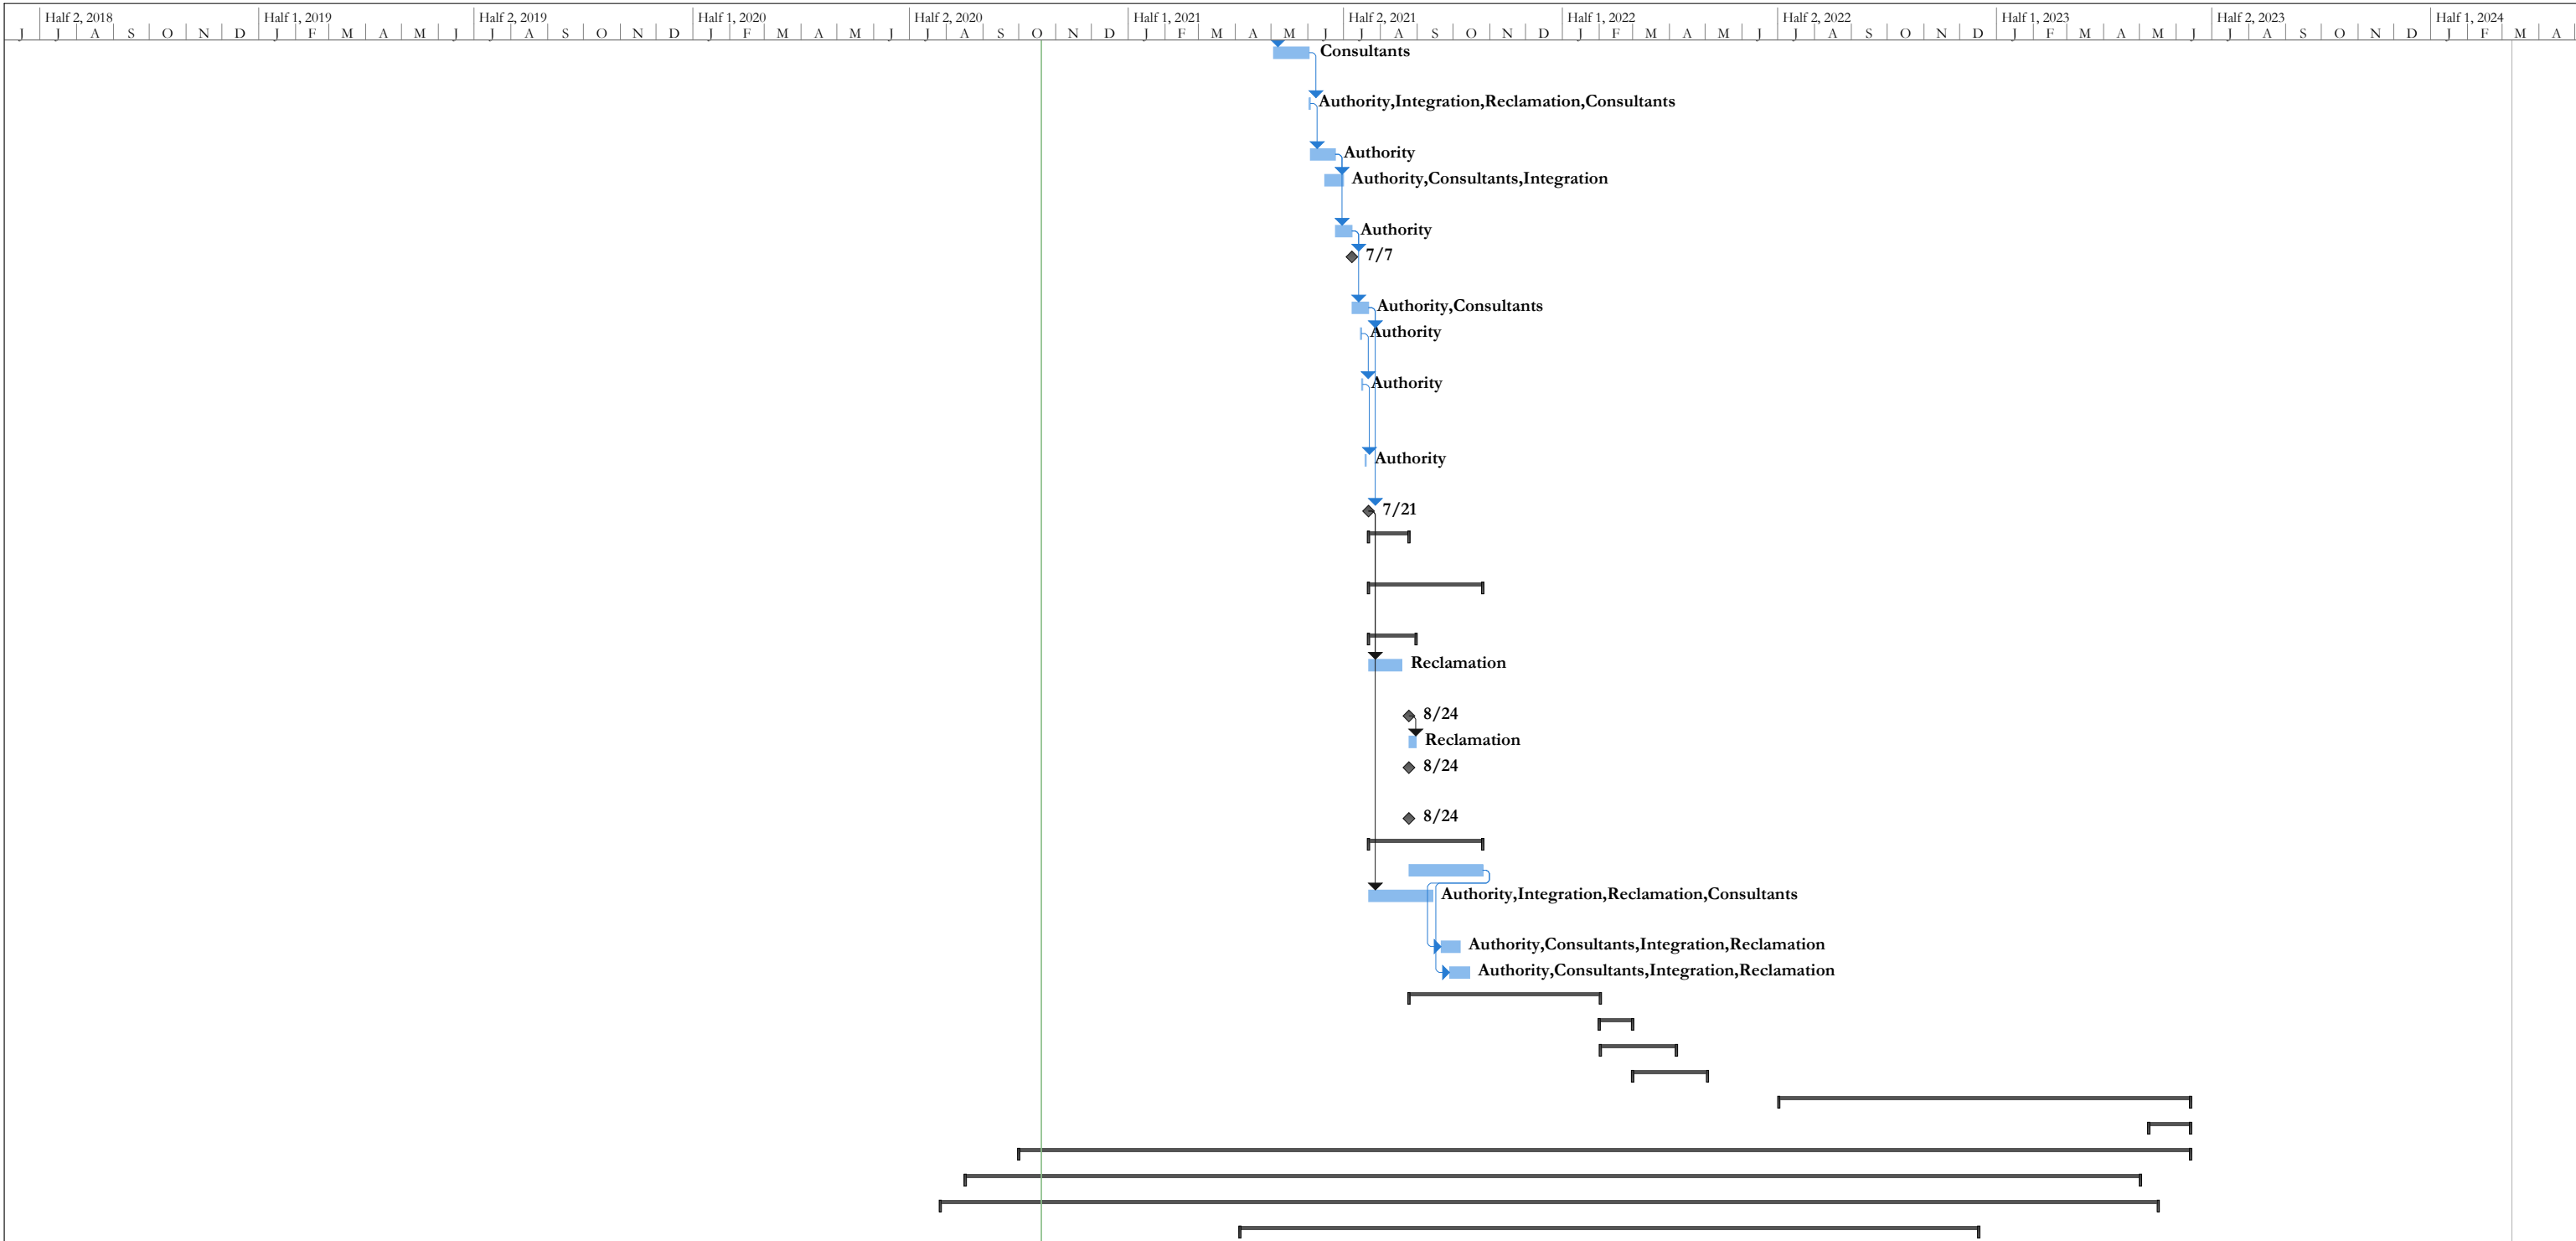

Project: DRAFT_Sites_Constrain
Date: Tue 10/20/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			
